


CRONOGRAMA DE EJECUCION DE AZLOR

DESCRIPCION	INICIO	DURACION	FINAL
Letrero en obra	1/12/2023	1	2/12/2023
Replanteo	1/12/2023	1	2/12/2023
Tarrancho	1/12/2023	1	2/12/2023
Estudio de Suelo	2/12/2023	5	7/12/2023
Caseta de Materiales	7/12/2023	3	10/12/2023
Fulmigacion	10/12/2023	1	11/12/2023
MOVIMIENTO DE TIERRA			
Remoción de capa Vegetal y Movimiento de Tierra	11/12/2023	3	14/12/2023
Bote de Material de Terrenos : F = 1.25	14/12/2023	2	16/12/2023
Exc De Zap de Cols (8 Unid)	16/12/2023	3	19/12/2023
Exc De Zap de Muros	16/12/2023	3	19/12/2023
Relleno Compactado : F = 1.45	19/12/2023	2	21/12/2023
Teflond en Material Granular en Zapatas	19/12/2023	2	21/12/2023
Rellenos de Material Extraídos	19/12/2023	2	21/12/2023
HORMIGON ARMADO			
Zap de Muros B = 0.60 mts (69.8 m)	21/12/2023	2	23/12/2023
Zap de Muros B = 0.45 mts (4.80 m)	21/12/2023	1	22/12/2023
Zap de Col C2 (1.20 x 1.40 x 0.35) 16 Unid	21/12/2023	1	22/12/2023
Zap de Col C2 (1.20 x 1.30 x 0.30) 4 Unid	21/12/2023	1	22/12/2023
Col C 2 (20 x 40) con 8 1/2" , 16 Unid	22/12/2023	1	23/12/2023
Col C 2 (20 x 30) con 6 1/2" , 4 Unid	22/12/2023	1	23/12/2023
Vigas de Amarres (20 x 20) con 4 Ø 3/8"	23/12/2023	1	24/12/2023
Vigas de Amarres (15 x 20) con 4 Ø 3/8" B N	23/12/2023	1	24/12/2023
Vigas de Amarres (15 x 20) con 4 Ø 3/8" S N	23/12/2023	1	24/12/2023
Platea t = 0.10 m con Aceros normal	24/12/2023	3	27/12/2023
D1 (15 * 20) con 5 Ø 3/8"	23/12/2023	1	24/12/2023
D2 (15 * 20) con 3 Ø 1/2"	23/12/2023	1	24/12/2023
MUROS S N P :			
Muros en Block de 8 " BNP	23/12/2023	4	27/12/2023
Muros en Block de 6 " BNP	23/12/2023	1	24/12/2023
Muros en Block de 6 " SNP	23/12/2023	8	31/12/2023
Muros en Block de 4 " en mesanina			
PAÑETES			
Fraguache con Escobas	31/12/2023	1	1/1/2024
Repello	31/12/2023	1	1/1/2024
Pañete en Pared Exterior	1/1/2024	2	3/1/2024
Pañete en Pared Interior	1/1/2024	1	2/1/2024
Mocheta	2/1/2024	1	3/1/2024
Cantos	3/1/2024	1	4/1/2024
Pañete en Columnas Rect	1/1/2024	1	2/1/2024

Empañetes en Dinteles	1/1/2024	1	2/1/2024
PISOS			
Pisos de Ceramica (0.50 * 0.50)	3/1/2024	2	5/1/2024
Zocalo de Ceramica (0.50 * 0.07)	5/1/2024	2	7/1/2024
Pisos de Ceramica 0.50 * 0.50) Tarima	5/1/2024	1	6/1/2024
Zocalo de Ceramica (0.50 * 0.07) Tarima	6/1/2024	1	7/1/2024
Pisos de Ceramica (0.50 * 0.50) Oficina	5/1/2024	1	6/1/2024
Pisos de Ceramicas (0.50 x 0.50) Sacristia	5/1/2024	1	6/1/2024
VENTANA			
V 1 (1.30 * 1.10) 2 Unid. Correderas	2/1/2024	2	4/1/2024
V 2 (1.20 * 1.10) 15 Unid. Correderas	2/1/2024	4	6/1/2024
PORTAJE			
P 1 (1.60 * 2.10) 1 Unid en MDF Batiente	2/1/2024	1	3/1/2024
P 2 (0.90 * 2.10) 2 Und en Polimetal	2/1/2024	1	3/1/2024
P5 (2.05 * 1.10) 1 und en Enrollables en Tarima	2/1/2024	1	3/1/2024
PINTURA			
Base	2/1/2024	2	4/1/2024
Pintura Pared Exterior e Interior	4/1/2024	3	7/1/2024
Pintura de Techo en Maderas	4/1/2024	2	6/1/2024
TERMINACION DE TECHO			
Vigas en Maderas 4" x 10" por 10 pies	1/1/2148	2	3/1/2148
Vigas en Maderas 4" x 8" por 10 pies	1/1/2148	2	3/1/2148
Vigas en Maderas 3" x 6" por 10 pies	1/1/2148	1	2/1/2148
Vigas en Maderas 1" 4" * 10 pies (Durmientes	1/1/2148	2	3/1/2148
Piezas en Aceros Grandes	3/1/2148	2	5/1/2148
Piezas en Aceros Pequeñas	3/1/2148	3	6/1/2148
Material Gastables (Clavos + antioxidos, etc.)	3/1/2148	3	6/1/2148
Aluzin Calibre 22	6/1/2148	3	9/1/2148
Calñerías horizontal	9/1/2148	1	9/1/2148
Caballetes horizontal	9/1/2148	1	10/1/2148
ELECTRICIDAD			
Salidas de Luces de Techo	10/1/2148	2	12/1/2148
Salidas de Luces de Pared	10/1/2148	2	12/1/2148
Salida de Interruptores Sencillos	10/1/2148	1	11/1/2148
Salida de Interruptores Doble	10/1/2148	1	11/1/2148
Salida de Interruptor TRW	10/1/2148	1	11/1/2148
Salida de Interruptores Piloto	10/1/2148	1	11/1/2148
Salida de tomacorriente de 110V	10/1/2148	1	11/1/2148
Salida de tomacorriente de 210V	10/1/2148	1	11/1/2148
Salida de Tomacorriente 110 S M	10/1/2148	1	11/1/2148

Salida de Tomacorriente 110 Indep	10/1/2148	1	11/1/2148
Panel de Distribución de 12 circuito	10/1/2148	1	11/1/2148
Salida Telf.	10/1/2148	1	11/1/2148
Salida TV	10/1/2148	1	11/1/2148
Salida de Timbre	10/1/2148	1	11/1/2148
Acometdias Telefonica	11/1/2148	2	13/1/2148
Acometdias TV	11/1/2148	2	13/1/2148
Acometida de Timbre	11/1/2148	2	13/1/2148
Registro Elec. (12" * 12 * 4") Telefono	11/1/2148	1	12/1/2148
Registro Elec. (12" * 12 * 4") TV	11/1/2148	1	12/1/2148
Registro Elec. (6" * 6 * 4") Inversor	11/1/2148	1	12/1/2148
Registro Elec. (6" * 6 * 4") Intercom	11/1/2148	1	12/1/2148
Registro Elec (12" * 12" * 6") de Electrico	11/1/2148	1	12/1/2148
Acometida Elect. 2 THW # 6 + 1 THW # 8	11/1/2148	1	12/1/2148
INSTALACIÓN SANITARIA:			
Inodoros Con Tapas	2/1/2024	3	5/1/2024
Lavamanos Sencillos	2/1/2024	3	5/1/2024
Desague de Piso	2/1/2024	2	4/1/2024
Colocacion de Tuberia Exterior	4/1/2024	3	7/1/2024
Construccion Camara de Impeccion	4/1/2024	4	8/1/2024
Camara Septica y Filtrantes	8/1/2024	6	14/1/2024
MISCELANEOS :			
Traslados de materiales en la obra	1/12/2023	45	15/1/2024
Limpieza Final	1/12/2023	45	15/1/2024

Rosa Lina Valdez

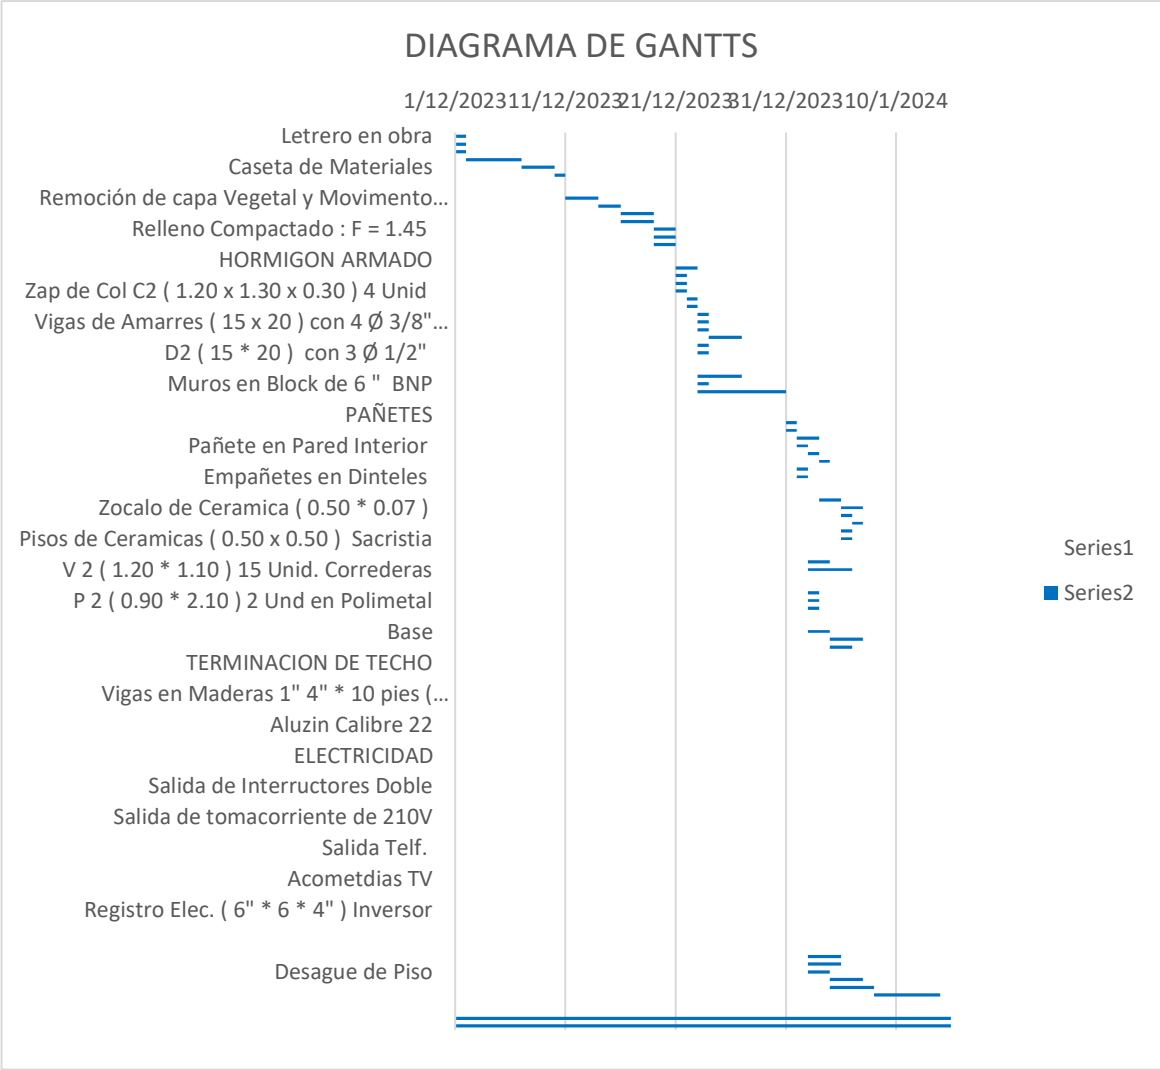

Rosa Lina Valdez
